

Work Order ID 70924

Friday, June 17, 2011 1:38:05 PM



Page 1

Item ID: D3166-1

Accept



Setup Start



Revision ID:

Stop



Item Name: Basket Hoop

Start Date: 6/17/2011 Start Qty: 12.00



Cust Item ID:

Required Date: 6/17/2011 Req'd Qty: 12.00



Customer:

Reference:

Approvals:

Process Plan:

H

Date: 11-06-17

Tooling:

Date:

QC:

Date:

SPC (Y/N):

Date:

Run Start



Stop



Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D3166	Rev A1

100

0.00



Skidtubes

Large Fab

Memo

0.00

Large Fab

Cut 3/4" x 3/4" square tubing 60.00" long.

SAO 11-07-14

(12)

110

0.00



BENDING MACHINE - SKIDTUBES

CNC Bend I

Memo

0.00

CNC Delta 100 Bender

Form D3166-1 Basket Hoop as per Dwg D3166 using Bending program 350 BASB, and folio 18.

DP
NW

11

11

P/O

11-07-29

120

0.00



QC6- Inspect dimensions to drawing

QC

Memo

0.00

Quality Control

Inspect Basket Hoop dimensions with template D3166-1-T1 (DT8302)

Suloslor

(11)

(11)

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: D3166-1 PAR #: N/A Fault Category: Small 9 Feb NCR: Yes ☒ No ☐ DQA: [Signature] Date: 9/16/2011
 Resolution: Scrap Disposition: Scrap QA: N/C Closed: [Signature] Date: 11/08/10

NCR: <u>70924</u>		WORK ORDER NON-CONFORMANCE (NCR) <u>#18.54</u>						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			
11-7-29	110	1 pc. kept slipping in Roller, under bent comt Repair PC process	<u>[Signature]</u>	Scrap 1 pc. NO replace.	<u>[Signature]</u> 11-8-2	<u>[Signature]</u> u66/02	<u>[Signature]</u>	<u>[Signature]</u> 11-08-02

NOTE: Date & initial all entries

Work Order ID 70924

Friday, June 17, 2011 1:38:05 PM



Page 2

Item ID: D3166-1

Accept



Setup Start



Revision ID:

Stop



Item Name: Basket Hoop

Start Date: 6/17/2011 Start Qty: 12.00



Cust Item ID:

Required Date: 6/17/2011 Req'd Qty: 12.00



Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start



QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop

Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

130

Identify as per dwg & Stock Location: CUA

0.00

SAD

11-08-03

(11)



Packaging

Memo

0.00

Packaging

140

QC21- Final Inspection - Work Order Release

0.00



QC

Memo

0.00

Quality Control

CK 11/08/03

11-08-3
(11)

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

Friday, June 17, 2011 1:38:15 PM

Page 1

Work Order ID: 70924



Parent Item: D3166-1



Parent Item Name: Basket Hoop

Start Date: 6/17/2011

Required Date: 6/17/2011

Start Qty: 12.00

Required Qty: 12.00

Comments: IPP A 02.08.23 New issue KJ
IPP: B 08.12.05 Updated bending program on step 3 per NCR W/O43165 KJ
Verified by: EC
IPP Rev: C 09-01-23 as per DEO D3166-A2 DD verified by: EC

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M304TS0.750W.065 		Purchased	No			100	f	790.7793	5	63.15789			
304 SQ Tube .75x.75x.065W												SAD 11-07-14	

Location

Loc Qty

Loc Code

MAT018

676.9243

117598

599.2256

117636

77.6987

WA007

113.8549906

116267

99.549272

116763

14.3057186

63.1579

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____


Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

DART


DESIGN #	DRAWN BY CP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED #	APPROVED #	DRAWING NO. D3166	REV. A SHEET 1 OF 1
DATE 02.07.10		TITLE BASKET HOOP	SCALE NTS
A	02.07.10	NEW ISSUE	
A1	04.04.08	38+/-1 WAS 36.0	

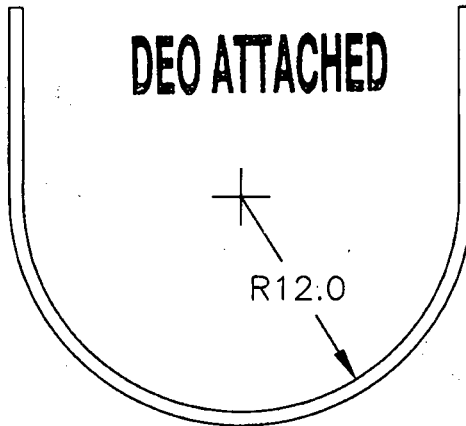RELEASED
02.08.06**DEO ATTACHED**

10.6 (REF, NEED 8.0 MIN)

D3166-1 BASKET HOOP

- 1) MATERIAL: AISI 304/316 SS SQUARE TUBING,
0.75" x 0.75" x 0.063 WALL, 60.00" LONG
(REF DART SPEC. M304TS0.750W.063)
- 2) FINISH: NONE
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS
OTHERWISE NOTED

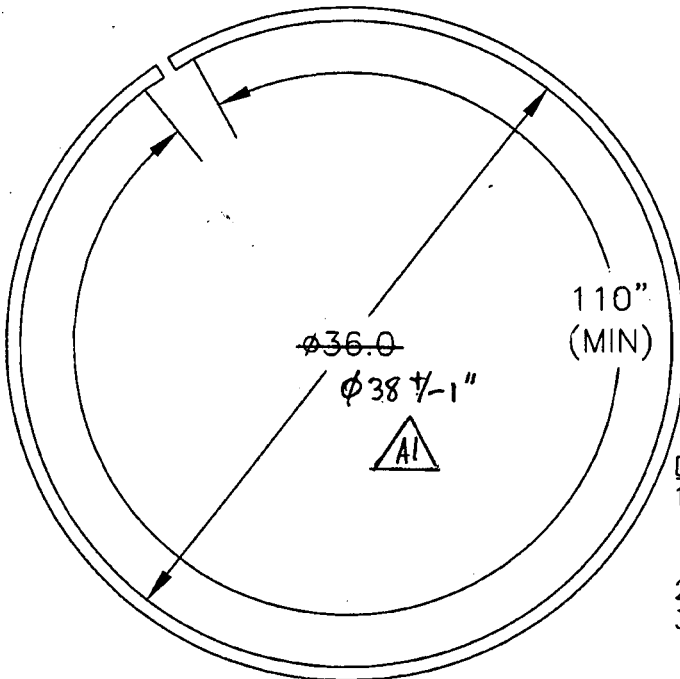

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 70924

P/11-06-17

D3166-3 BASKET HOOP

- 1) MATERIAL: AISI 304/316 SS SQUARE TUBING,
0.75" x 0.75" x 0.063 WALL, 120.00" LONG
(REF DART SPEC. M304TS0.750W.063)
- 2) FINISH: NONE
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS
OTHERWISE NOTED

Copyright © 2002 by DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

DRAWING NO. D3166	TITLE BASKET HOOP	REV A1	DART AEROSPACE LTD ENGINEERING ORDER		D.E.O. NO. D3166-A-2	SHEET NO. 1 OF 1	SCALE NTS
DRAWN AJS	CHECKED <i>[Signature]</i>	MFG. APPR. <i>[Signature]</i>	APPROVED <i>[Signature]</i>		DE APPR. <i>[Signature]</i>		
DATE 08.12.11	DATE 08.12.15	DATE 08/12/15	DATE 08/12/16		DATE 08.12.16		

1) MODIFY MATERIAL NOTE FOR D3166-1 AS SHOWN:

IS:

- 1) MATERIAL: AISI 304/316 SS, 3/4 X 3/4 X 0.065 WALL SQUARE TUBING,
60.00" LONG
REF. DART SPEC M304TS0.750W.065

WAS:

- 1) MATERIAL: AISI 304/316 SS SQUARE TUBING,
0.75" x 0.75" x 0.063 WALL, 60.00" LONG
(REF DART SPEC. M304TS0.750W.063)

w/o 70924

2) MODIFY MATERIAL NOTE FOR D3166-3 AS SHOWN:

IS:

- 1) MATERIAL: AISI 304/316 SS, 3/4 X 3/4 X 0.065 WALL SQUARE TUBING,
120.00" LONG
REF. DART SPEC M304TS0.750W.065

WAS:

- 1) MATERIAL: AISI 304/316 SS SQUARE TUBING,
0.75" x 0.75" x 0.063 WALL, 120.00" LONG
(REF DART SPEC. M304TS0.750W.063)

RELEASED
08/12/16 *[Signature]*

REASON: SEE PAR 08-005

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries
